



CDU Self Qualification Guidelines

Application Note

Document History

Version	Date	Authors	Description of Change
01	September 19, 2025	BE, PS, PH, DL	Initial release
02	April 20, 2026	BE, PS, PH, DL	“Quality Management” section has been updated
03	September 21, 2026	BE, SK	➤ Added NVIDIA DSX-Ready requirements section ➤ Removed Business and Supply Chain Readiness section ➤ Removed Quality and Reliability section

Table of Contents

Introduction.....	1
General Expectations.....	1
CDU Qualification Overview.....	2
Step 1: Product Requirements Document Review.....	2
Step 2: Wetted Materials Compatibility.....	2
Step 3: Core Requirements Availability.....	3
Step 4: Qualification Tests.....	5
Test 1: Hydraulic Test - Constant Differential Pressure.....	5
Test 2: Hydraulic Test - Constant Flow Rate Mode.....	6
Test 3: Telemetry Verification Test – Flow Sensor Accuracy.....	7
Test 4: Cold Start Thermal Test.....	8
Test 5: Thermal Test – Low Load.....	8
Test 6: Thermal Test – Nominal Capacity.....	9
Test 7: Pump Failover.....	11
Test 8: Fan Failover.....	12
Test 9: CDU Group Control.....	12
Test 10: Pumping Capacity.....	13
DSX-Ready Qualification.....	15
DCE MEP Equipment Qualification Process.....	17
Step 1: Login to NVOnline.....	17
Step 2: Navigate to Report a Bug.....	18
Step 3: Fill in the Bug Report Form.....	18
Step 4: Enter CDU-Specific Description (Qualification Review).....	20
Step 4 (Alternate): Enter CDU Description for RFI.....	20
Step 5: Add Members, Upload Attachments, and Submit.....	20
Step 6: View Bug Status and Add Comments.....	22
Flushing Procedure.....	24
Executive Summary.....	24
Detailed Flushing Steps.....	25
Filter Initial Inspection.....	26
Looping and Charging.....	26
Flushing with Coolant.....	26
Draining and Inspecting.....	27

List of Figures

Figure 1. Flushing Steps.....	19
Figure 2. Filter Inspection.....	20
Figure 3. Connecting Unit Coolant Supply Port.....	20

List of Tables

Table 1. CDU Qualification Example.....	2
Table 2. Core Requirements.....	3
Table 3. ATDs for CDU Type.....	10

Introduction

This application note serves as a guideline for the qualification process of coolant distribution units (CDUs) conducted at the vendor's site. The goal is to verify the availability and functionality of key requirements for in-row L2L and L2A CDUs, including hydraulic performance, thermal capacity, telemetry, wetted materials, safety, redundancy, and failure response strategy. Once the process is complete, all test data must be submitted using the provided template for NVIDIA review and approval. Any changes to the requirements must be reviewed and approved by the owner's representatives.

General Expectations

Vendors are advised to thoroughly review the instructions outlined in this application note to ensure a comprehensive understanding of the steps involved in the process. Submissions are expected to be clear, well-written, and accurate. Acronyms must be defined upon first use. The provided data template must be followed, and the required raw data for each test must be included. Any additional considerations may be added directly to the relevant section for each test.

CDU Qualification Overview

This section provides an overview of the process, from product requirements document (PRD) review to RVL listing.

Step 1: Product Requirements Document Review

The vendor must respond to each item outlined in the "CDU Requirements" document, clearly indicating whether their design complies with each requirement. For any deviations, the vendor should specify whether there are plans to meet the stated requirement at a later time, or propose available alternative solutions.

Reference document: "CDU Requirements Document"

Table 1. CDU Qualification Example

Required ID	Item	Description	Response from Vendor
CONT-REQ-01	Constant differential pressure mode	The unit shall support operation using differential pressure on the secondary flow loop. The differential pressure set point shall be remotely settable.	Compliant/non-compliant (For non-compliant items, provide current design details and note any planned updates or alignment)

Step 2: Wetted Materials Compatibility



Vendors must complete the wetted materials table in the provided template (**Report_Template.xlsx**), specifying all materials used in their CDU. A comprehensive list of approved materials for metals, rubbers, plastics, sealants, lubricants, and brazing materials is provided as a guideline.

To access the attached file, click the Attachment icon on the left-hand toolbar on this PDF (using Adobe Acrobat Reader or Adobe Acrobat). Select the file and use the Tool Bar options (Open, Save) to retrieve the document.

Step 3: Core Requirements Availability

A subset of the requirements has been designated as “Core Requirements,” representing the minimum essential features needed to successfully pass the qualification process. The test guidelines have been developed in accordance with the specified requirements. These requirements are outlined in the following table. Vendors must complete the “Core Requirements Checklist” in the provided template at the end of this application note.

Table 2. Core Requirements

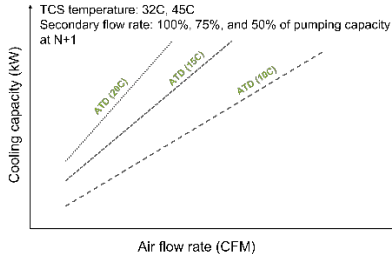No.	Core Requirement	Requirement ID	L2A CDU	L2L CDU
1	Cooling capacity	THERM-REQ-01	Minimum recommended capacity is 70 kW (for single-wide, 600mm) and 135 kW (for double-wide, 1200mm) at a 10 °C approach temperature at the minimum required coolant flow rate and pressure differential defined at PUMP-REQ-01 and PUMP-REQ-01 Cooling curve: 	Minimum recommended capacity is 2.3 MW at a 4 °C approach temperature at the minimum required coolant flow rate and pressure differential defined at PUMP-REQ-01 and PUMP-REQ-02 Cooling curve: 
2	Secondary temperature stability	THERM-REQ-02	The unit shall support a stable secondary set-point temperature of $\leq 45\text{ °C} \pm 1\text{ °C}$ for a baseline load of 10% of the maximum load (at 10°C ATD) to 100% of the maximum load (at 10°C ATD).	The unit shall support a stable secondary set-point temperature range of $\leq 45\text{ °C} \pm 1\text{ °C}$ for a baseline load of 10% of the maximum load (at 4°C ATD) to 100% of the maximum load (at 4°C ATD).
3	Pumping capacity at required cooling capacity	PUMP-REQ-01 PUMP-REQ-02	The unit should provide a minimum flow rate of 1.5 LPM/kW at the minimum recommended cooling capacity (THERM-REQ-01).	The unit should provide a minimum flow rate of 1.5 LPM/kW at the minimum recommended cooling capacity (THERM-REQ-01).
4	Pump	PUMP-	CDU Should have N+1	CDU should have N+1

No.	Core Requirement	Requirement ID	L2A CDU	L2L CDU
	redundancy	REQ-04	redundancy for pumps.	redundancy for pumps.
5	Fan redundancy	FAN-REQ-04	CDU shall have N+1 redundancy for fans.	Not applicable
6	Secondary filter	FILT-REQ-02	The CDU shall support 25 µm filter with no filter housing changes required. Secondary filters shall have N+1 redundancy.	The CDU shall support 25 µm filter with no filter housing changes required. Secondary filters shall have N+1 redundancy.
7	Pump field replacement	SERV-REQ-01	The pump shall be hot swappable with no system downtime.	The pump shall be hot swappable with no system downtime.
8	Fan field replacement	SERV-REQ-02	The fan shall be hot swappable with no system downtime.	Not applicable
9	Pressure Relief Valve (PRV) setpoint	SAFE-REQ-03	The unit shall have a PRV to prevent any damage in the presence of high working pressure. Set point pressure is 6 bar.	The unit shall have a PRV to prevent any damage in the presence of high working pressure. Set point pressure is 6 bar.
10	Constant differential pressure mode	CONT-REQ-01	The unit shall support operation using differential pressure on the secondary flow loop. The differential pressure set point shall be remotely settable.	The unit shall support operation using differential pressure on the secondary flow loop. The differential pressure set point shall be remotely settable.
11	Constant flow rate mode	CONT-REQ-02	The unit shall support operation using constant flow rate mode on the secondary flow loop. The flow rate set point shall be remotely settable.	The unit shall support operation using constant flow rate mode on the secondary flow loop. The flow rate set point shall be remotely settable.
12	Telemetry (sensor connection verification)	TELE-REQ-01	The unit shall support real-time monitoring for all the main parameters (flow rate, temperature, pressure, and level sensor)	The unit shall support real-time monitoring for all the main parameters (flow rate, temperature, pressure, and level sensor)
13	Flow sensor accuracy - TCS loop	SENS-REQ-01	Flow sensor shall be calibrated for Recochem's PG25 (25% propylene glycol/water) to $\pm 5\%$ of the full-scale It is recommended to use an electromagnetic flow sensor due to its superior accuracy.	Flow sensor shall be calibrated for Recochem's PG25 (25% propylene glycol/water) to $\pm 3\%$ of the full-scale It is recommended to use an electromagnetic flow sensor due to its superior accuracy.
14	Flow sensor	SENS-REQ-02	They shall be calibrated for	They shall be calibrated for

No .	Core Requirement	Requirement ID	L2A CDU	L2L CDU
	accuracy - Primary loop		water to $\pm 5\%$ of the full-scale for each specific CDU type	water to $\pm 5\%$ of the full-scale for each specific CDU type
15	Pump failover	PUMPFAIL-REQ-01 to 04	If one pump fails, the transition time to another pump shall occur within 5 seconds or less.	If one pump fails, the transition time to another pump shall occur within 5 seconds or less.
16	Fan failover	FANFAIL-REQ-01 to 02	If one fan fails, the transition time to another fan shall occur within 5 seconds or less.	Not applicable
17	Group control	GCONT-REQ-01 to 04	If one CDU fails, the transition time to another CDU shall occur within 5 seconds or less.	If one CDU fails, the transition time to another CDU shall occur within 5 seconds or less.

Step 4: Qualification Tests

This section outlines the details of each test, including its scope and the steps involved. All parameter setpoints are defined, with references to the corresponding tab in the template where test data must be provided.

This section starts with an overall review of setup instrumentation requirements, and flushing procedure.

Instrumentation of the setup and external sensors requirements:

- > Flow Sensor with accuracy of $\pm 0.5\%$ of reading
- > Temperature Sensor – Type T ($\pm 1.0^\circ\text{C}$ or $\pm 0.75\%$)
- > Pressure Sensors- $\pm 0.25\%$ to $\pm 1.0\%$ of full scale

Flushing Procedure:

- > Flush the CDU before starting the test.
- > A flushing procedure is provided in Appendix A as a guideline.
- > Share the flushing procedure followed for your test with Nvidia.

Test 1: Hydraulic Test - Constant Differential Pressure

This section outlines the procedures and performance expectations for operating the CDU in constant differential pressure (DP) mode. In this control mode, the CDU maintains a fixed pressure difference across the secondary loop to ensure stable and consistent flow, regardless of downstream fluctuations. The following tests aim to verify the CDU's ability to deliver stable flow across a range of operating conditions.

Test Steps:

1. Configure the CDU to operate under constant differential pressure (DP) mode as defined in the system settings.
2. Set the CDU to operate at multiple DP setpoints: 20 psi, 25 psi, 30 psi, and 35 psi. At each setpoint, allow the system to respond and stabilize, and monitor its performance (for example, DP, flow rate, and any system alarms or faults).
3. If any of the specified DP setpoints are unsupported by the CDU or do not fall within the operational range, this should be documented in the report along with an explanation of the limitation.
4. Record the stabilization time for each DP setpoint. Start timing from the moment the new DP setpoint is applied and capture the time when the system reaches steady state condition.
5. Maintain operation at each setpoint after reaching a steady state:
 - a. For L2L CDUs, continue the test for at least 5 minutes after stabilization.
 - b. For L2A CDUs, continue for at least 15 minutes.
 - i. During this period, observe for fluctuations, alarm triggers, and consistent sensor readings.
6. Ensure effective stabilization, meaning the CDU maintains its target setpoint and key performance parameters (DP and flow rate) remain stable across all test conditions without oscillation or drift.
7. Record data from all available pressure, temperature, and flow sensors within the CDU during each test to verify sensor functionality and data integrity.
8. Record data from all available external pressure, temperature, and flow sensors during each test to verify CDU's sensors functionality and accuracy.
9. The data sampling rate should be at least once per two seconds throughout the test to ensure accurate trend analysis and post-test validation.
10. Provide the test data in the specified tab, "Test 1," in the template.

Test 2: Hydraulic Test - Constant Flow Rate Mode

This section describes the procedures and performance criteria for operating the CDU in constant flow rate mode. In this mode, CDU maintains a fixed secondary loop flow rate, regardless of pressure changes in the system. The following tests aim to verify the CDU's ability to deliver stable flow across a range of operating conditions.

Test Steps:

1. Configure the CDU to operate under constant flow rate mode as defined in the system settings.
2. Set the CDU to operate at multiple flow rate setpoints: 25%, 50%, 75%, and 100% of the nominal flow rate. At each setpoint, allow the system to respond and stabilize, and monitor its performance (for example, DP, flow rate, and any system alarms or faults).
3. Record the stabilization time for each flow rate setpoint. Start timing from the moment the new setpoint is applied and capture the time when the system reaches steady state condition.
4. Maintain operation at each setpoint after reaching a steady state:

- a. For L2L CDUs, continue the test for at least 5 minutes after stabilization.
 - b. For L2A CDUs, continue for at least 15 minutes.
 - i. During this period, observe for fluctuations, alarm triggers, and consistent sensor readings.
5. Ensure effective stabilization, meaning the CDU maintains its target setpoint and key performance parameters (DP and flow rate) remain stable across all test conditions without oscillation or drift.
6. Record data from all available pressure, temperature, and flow sensors within the CDU during each test to verify sensor functionality and data integrity.
7. Record data from all available external pressure, temperature, and flow sensors during each test to verify CDU's sensors functionality and accuracy.
8. The data sampling rate should be at least once per two seconds throughout the test to ensure accurate trend analysis and post-test validation.
9. Provide the test data in the specified tab, "Test 2," in the template.

Test 3: Telemetry Verification Test – Flow Sensor Accuracy

This test is conducted to verify the accuracy of the flow sensor under controlled conditions. The measured flow rates will be compared against reference values obtained from a calibrated flow meter. The goal is to ensure the sensor meets the required accuracy specifications across the expected operating range.

Test Steps:

1. Select a calibrated and accurate external flow sensor to serve as the reference for this test. The selected sensor must have a minimum accuracy of $\pm 0.5\%$ of reading and be calibrated for PG25 fluid conditions. Recommended sensor types include Coriolis or Electromagnetic flow meters. Specify the sensor type, model, and calibration certificate and reference in the report.
2. Document the type of internal flow sensor used in the CDU on the secondary side, including manufacturer, model, and stated accuracy.
3. Configure the CDU to operate in constant flow rate mode and test it at 4 flow rate setpoints including 10%, 50%, 75%, and 100% of the nominal (rated) secondary flow rate.
4. At each flow rate setpoint, run the CDU at three TCS supply temperatures to observe any temperature-dependent variation
 - a. 25°C
 - b. 35°C
 - c. 45°C
5. Record and compare flow readings from both the internal CDU sensor and the external reference sensor at each combination of flow rate and temperature. Maintain steady-state conditions before taking the readings to ensure data consistency.
6. Repeatability Check: Optionally, repeat each test point at least twice to verify consistency and repeatability of internal sensor readings under the same conditions.

7. Provide the test data in the specified tab, "Test 3," in the template.

Test 4: Cold Start Thermal Test

The objective of this test is to verify that the temperature control PID loop does not experience loop windup (accumulated error) that could hinder timely valve response during a cold start.

Test Steps:

1. Start the CDU with no heat load applied, only the pumps operating. Ensure the CDU secondary supply temperature is at least 2°C below the setpoint (with the primary valve fully closed) and maintain this condition for 30 minutes before starting the test.
2. Apply a 50% heat load to the CDU. Monitor the secondary supply temperature and observe it gradually increasing and approaching the setpoint.
3. Confirm that the primary valve begins to modulate open either:
 - a. Just before the secondary supply temperature reaches the setpoint, or
 - b. Within 10 seconds after the secondary supply temperature exceeds the setpoint.
4. Once the system stabilizes, ensure that the secondary supply temperature remains within $\pm 1^\circ\text{C}$ of the setpoint.
5. Step 3 serves as the pass or fail criterion. If the primary valve fails to open within the required time window, the CDU does not meet the control response requirements.
6. Provide the test data in the specified tab, "Test 4," in the template.

Test 5: Thermal Test – Low Load

The objective of this test is to evaluate the CDU's ability to maintain a stable and uniform TCS temperature setpoint under low-load conditions.

Test Steps:

1. Set the CDU to operate in constant differential pressure (DP) mode as defined in system settings.
2. Fine-tune the DP setpoint so the secondary flow rate reaches 50% of the nominal flow.
3. Configure the CDU to maintain a TCS supply coolant temperature of 30°C.
4. Gradually introduce heat load until it reaches 10% of the rated capacity.
5. Record the stabilization time, starting from heat load application until the system reaches steady state condition.
6. At steady state, monitor the CDU secondary supply coolant temperature and confirm that temperature fluctuations remain within $\pm 1^\circ\text{C}$ of the 30°C setpoint.
7. If temperature fluctuations exceed $\pm 1^\circ\text{C}$, fine-tune the PID control parameters to improve stability and response.
8. Once stabilized, continue the test as required:
 - a. For L2L CDUs, continue the test for at least 5 minutes after stabilization.

- b. For L2A CDUs, continue for at least 15 minutes.
 - i. During this period, observe for fluctuations, alarm triggers, and consistent sensor readings.
9. Provide the test data in the specified tab, “Test 5,” in the template.

Test 6: Thermal Test – Nominal Capacity

Section 1: This section looks for validation of the nominal cooling capacity of the CDU at 4°C ATD for L2L CDUs and 10°C ATD for L2A CDUs. The test covers two pump and fan configuration modes:

- > N+1 mode (one pump/fan in standby)
- > All pumps/fans running (no standby)

Test Steps:

1. Set the CDU to operate with N pumps and fans running and 1 pump or fan on standby.
2. Set the CDU to operate in constant differential pressure (DP) mode as defined in system settings.
3. Fine-tune the DP setpoint so the secondary flow rate reaches 100% of the nominal flow.
4. Adjust the primary flow rate to its maximum, which corresponds to the maximum recommended differential pressure (DP) of 20 psi on the primary side (HX-REQ-02). If achieving the requested maximum flow rate is not possible, use the highest available primary flow rate and clearly indicate this in the result section.
5. Configure the CDU to maintain a TCS supply coolant temperature of 30°C (TCS temperature can be higher at 40°C for L2A CDUs if lower is not possible).
6. Gradually introduce heat load until it reaches 100% of the rated capacity at 4°C ATD.
7. Record the stabilization time, starting from heat load application until the system reaches steady state.
8. At steady state, monitor the CDU secondary supply coolant temperature and confirm that temperature fluctuations remain within $\pm 1^\circ\text{C}$ of the 30°C setpoint.
9. If temperature fluctuations exceed $\pm 1^\circ\text{C}$, fine-tune the PID control parameters to improve stability and response.
10. Once stabilized, continue the test as required:
 - a. For L2L CDUs, continue the test for at least 5 minutes after stabilization.
 - b. For L2A CDUs, continue for at least 15 minutes.
 - i. During this period, observe for fluctuations, alarm triggers, and consistent sensor readings.
11. If the heat load cannot meet the nominal capacity, clearly document this in the report and explain the limitation.
12. Repeat Step 2 through Step 10 with all pumps and fans running and no pump or fan in standby.
13. Provide the test data in the specified tab, “Test 6-1”, in the template.

Section 2: Provide cooling performance curves at the specified Approach Temperature Differences (ATDs) for each CDU type and validate them with test data. If some setpoints cannot be achieved due to insufficient available heat load, the remaining data points may be generated using heat exchanger modeling software. In such cases, the available test data must be used to verify the accuracy of the software-generated values.

Table 3. ATDs for CDU Type

CDU Type	ATD Setpoints	TCS Flow Rate (% of Rated Flow Rate at 100% Pump Speed)
L2A	10°C, 15°C, 20°C	50%, 75%, 100%
L2L	4°C, 8°C, 12°C	50%, 75%, 100%

Test Steps:

1. Configure the CDU to operate in constant flow rate mode as defined in the system settings.
2. Run this test with an N+1 pump or fan redundancy configuration, meaning one pump or fan being in standby mode.
3. Set the CDU to operate at multiple flow rate setpoints: 50%, 75%, and 100% of the nominal TCS flow rate. At each setpoint, allow the system to respond and stabilize, and monitor its performance (for example, DP, flow rate, and any system alarms or faults).
4. Adjust the TCS supply temperature setpoint to achieve the ATD for each test condition. The recommended TCS temperatures are 30°C and 40°C for L2L CDUs, and 40°C and 45°C for L2A CDUs.
5. Gradually introduce heat load until it reaches 100% of the rated capacity at each ATD.
6. Once steady-state conditions are reached, monitor the secondary supply temperature and ensure fluctuations remain within $\pm 1^\circ\text{C}$.
7. Record the maximum stable heat load achieved at each flow rate and ATD condition as the nominal cooling capacity for that test.
8. Specify the temperature and flow rate of the primary medium:
 - a. Water (or other fluid) for L2L CDUs
 - b. Air for L2A CDUs
9. If the heat load is insufficient to reach nominal capacity at a given ATD, clearly document this in the test report and explain the limitation (for example, available load, system constraints).
10. Provide the test data in the specified tab, "Test 6-2," in the template.

Test 7: Pump Failover

Section 1: This section examines the time required for the pumps to start up and reach their nominal flow rate capacity.

Test Steps:

1. Set the CDU to operate with N pumps running.
2. Configure the CDU to operate in constant differential pressure (DP) mode as defined in system settings.
3. Fine-tune the DP setpoint to achieve 100% of the nominal TCS flow rate.
4. Record the time required for the pumps to reach the nominal flow rate capacity.
5. Ensure the CDU reaches a steady state condition at the nominal flow rate.

Section 2: The objective of this test is to validate the CDU's ability to respond appropriately in a pump failover scenario. The test covers two pump configuration modes:

- > N+1 mode (one pump in standby)
- > All pumps running at lower speed (no standby)

Test Steps:

1. Set the CDU to operate with N pumps running and 1 pump on standby.
2. Configure the CDU to operate in constant differential pressure (DP) mode as defined in system settings.
3. Fine-tune the DP setpoint so the TCS flow rate reaches 100% of the nominal flow.
4. Configure the CDU to maintain a secondary supply coolant temperature of 30°C.
5. Gradually introduce heat load until it reaches 100% of the rated capacity at 4°C ATD.
6. If the heat load is insufficient, use the maximum available heat load, and document this in the test report along with the reason (for example, load bank limits, system constraints).
7. Wait until the system reaches steady-state conditions before simulating a failure. Key indicators should include stable DP, flow rate, and supply temperature.
8. Simulate a failure of the active pump and observe the system's behavior.
9. Monitor failover response by
 - a. Record the time it takes for the backup pump to start and ramp up.
 - b. Record the time required for the CDU to recover to its target DP, flow rate, and supply temperature.
 - c. Monitor and document any transient fluctuations in flow rate and supply temperature during the transition.
10. Repeat Step 2 through Step 9 with all pumps running at a reduced speed and no pump in standby.
11. Provide the test data in the specified tab, "Test 7," in the template.

Test 8: Fan Failover

The objective of this test is to validate the CDU's ability to respond appropriately in a fan failover scenario. The test covers two pump configuration modes:

- > N+1 mode (one fan in standby)
- > All fans running at lower speed (no standby)

Test Steps:

1. Set the CDU to operate with N fans running and 1 fan on standby.
2. Configure the CDU to operate in constant differential pressure (DP) mode as defined in system settings.
3. Fine-tune the DP setpoint so the TCS flow rate reaches 100% of the nominal flow.
4. Configure the CDU to maintain a secondary supply coolant temperature of 30°C.
5. If 30°C is not achievable due to air supply temperature constraints, target the minimum possible temperature and clearly state the new setpoint.
6. Gradually introduce heat load until it reaches 100% of the rated capacity at 10°C ATD.
7. If the heat load is insufficient, use the maximum available heat load, and document this in the test report along with the reason (for example, load bank limits, system constraints).
8. Wait until the system reaches steady-state conditions before simulating a failure. Key indicators should include stable DP, flow rate, and supply temperature.
9. Simulate a failure of one of the active fans and observe the system's behavior.
10. Monitor failover response by
 - a. Record the time it takes for the standby fan to start and ramp up.
 - b. Record the time required for the CDU to recover to its target DP, flow rate, and supply temperature.
 - c. Monitor and document any transient fluctuations in supply temperature or cooling performance during recovery.
11. Repeat Step 2 through Step 10 with all fans running at reduced speed and no fan in standby.
12. Provide the test data in the specified tab, "Test 8," in the template.

Test 9: CDU Group Control

To validate the group control functionality of CDUs operating in coordination. This test ensures the system can detect the failure of one CDU and automatically redistribute the load across the remaining units without compromising cooling performance.

The test is performed under the following two configurations:

- > N+1 configuration – One CDU is in standby mode
- > All CDUs are running at reduced capacity (no standby)

Test Setup:

- > Minimum of two or more CDUs configured in a group control scheme
- > Shared connection to the same TCS secondary loop

- > Each CDU is equipped with independent power and control, but operates with shared group logic

Test Steps:

1. Set multiple CDUs to operate in group control mode with active communication between units.
2. Define one CDU as the group leader, if applicable.
3. Confirm all CDUs are assigned roles and sharing load as designed.
4. Set the system to operate with N CDUs running and 1 CDU on standby.
5. Set all CDUs to operate in constant differential pressure mode.
6. Adjust setpoints so the running CDU provides 100% of the nominal secondary flow rate.
7. Set the TCS supply temperature setpoint to 30°C.
8. Gradually introduce heat load until it reaches 100% of the rated capacity at 10°C ATD.
9. If the heat load is insufficient, use the maximum available heat load, and document this in the test report along with the reason (for example, load bank limits, system constraints).
10. Wait until the system reaches steady-state conditions before simulating a failure. Key indicators should include stable DP, flow rate, and supply temperature.
11. Power off or simulate a fault in one of the active CDUs.
12. Observe system behavior and confirm the standby CDU activates and compensates for the failed unit.
13. Record system response for the following:
 - a. Time to activate standby CDU
 - b. Time to return to target flow, DP, and temperature
 - c. Any fluctuations in flow, DP, or temperature
 - d. Any alarms or faults triggered
14. Repeat Step 5 through Step 13 with all CDUs running at reduced speed and no CDU in standby.
15. Provide the test data in the specified tab, "Test 9," in the template.

Test 10: Pumping Capacity

The objective of this test is to verify the pump PQ (pressure vs. flow) curve and determine the available external pressure head. This test should be conducted using PG25 fluid conditions.

The test is performed under the following two configurations:

- > N+1 configuration – One pump is in standby mode
- > N configuration – All pumps running

Test Steps:

1. Set the CDU to operate with N pumps running and 1 pump on standby.
2. Use 25 micron secondary filter size.

3. Configure the CDU to operate at 100% pump speed (fixed speed) to generate a consistent PQ curve.
4. Adjust the DP setpoint or use external flow restriction to achieve multiple flow rates, covering the full operational range of the pump.
5. Specify what the CDU-reported DP represents:
 - a. Does it include internal impedance or is it limited to external loop DP?
 - b. What are the secondary filter sizes if different from 25 microns?
6. Use calibrated pressure sensors placed at the inlet and outlet of the CDU to measure the true external DP (that is, pressure head available to the loop).
7. Compare the CDU-reported DP with the externally measured DP at each flow rate.
8. Document any discrepancies and verify consistency with the expected PQ curve behavior.
9. Repeat Step 2 through Step 7 with all pumps running at 100% speed and no pump in standby.
10. Provide the test data in the specified tab, "Test 10," in the template.

DSX-Ready Qualification

This section defines the DSX-Ready qualification requirements and applies to CDUs seeking the DSX-Ready designation. It should be completed after successfully finishing all 10 tests in the preceding section. The information needed for the following requirements should be provided in the designated section of the report template.

The following core requirements must be satisfied:

1. Minimum cooling capacity of 2.3 MW at 4°C ATD. Cooling capacity data must be reported in Test 6-2, where full capacity measurements are presented.
2. Minimum flow rate of 1.5 LPM/kW. Flow rate availability is derived from the pumping capacity data reported in Test 10 and will be evaluated against the nominal cooling capacity at 4°C ATD.
3. Minimum differential pressure head of 45 psi (target: 50 psi) at the required flow rate and rated cooling capacity at 4°C ATD.
4. 6-inch flange connection for both supply and return lines.
5. Power consumption must not exceed 3% of the CDU's rated capacity.
6. Power feed compliant with regional power standards, supporting 380–415V and 480V at 50/60Hz.
7. Two-way modulating primary valve.
8. Regionally CE or UL certified.
9. Modbus TCP setpoint volatility control. The CDU secondary supply temperature setpoint must be adjustable via Modbus TCP and must immediately respond to each new setpoint without writing to non-volatile memory on every update, preventing memory burnout from high-frequency BMS writes (e.g., every 5 seconds). One compliant approach is to defer non-volatile memory writes until a setpoint has persisted for a minimum of 10 minutes.
10. MTBF and MTBR data must be provided for major components including pumps, VFDs, valves, power system (ETS/ATS), and control board.
11. CDU SimReady Asset. Vendors are expected to deliver a SimReady asset for the CDU in accordance with the requirements outlined above. A commitment to deliver the SimReady asset must be provided at the time of submission, with delivery to follow upon completion.
 - SimReady assets are OpenUSD-based digital replicas of liquid cooling components optimized for geometry accuracy, simulation metadata, and cross-tool interoperability within the Omniverse ecosystem.
 - They exist to enable AI Factory Digital Twin (AiF DT) construction at scale, allowing liquid cooling OEMs to contribute standardized component-level digital twins that can be aggregated into a unified data center simulation without bespoke integration work.
 - Each SimReady CDU asset carries structured metadata beyond geometry, including cooling capacity curves, flow rates, pump redundancy strategies, working fluid specs, and connection points encoded in OpenUSD attributes, making assets directly consumable by thermal and hydraulic simulation solvers.
 - NVIDIA is driving SimReady adoption for liquid cooling by enabling OEMs to produce simulation-ready CDU assets at the source via a CAD-to-OpenUSD pipeline (Scene Optimizer + Asset Validator).
 - Further information on SimReady asset can be found [here](#)

DCE MEP Equipment Qualification Process

This section outlines the process for partners to submit their CDU products for DCE's AI factory infrastructure qualification through the NVOnline NVBug system. The process covers two use cases: Qualification Review (for formal product qualification submissions) and Request for Information (RFI) (for pre-qualification questions and clarifications). Approved partner products will be listed in a published DC-Infrastructure partners document and celebrated through the NVIDIA Partner Network portal.


Step 1: Login to NVOnline

Navigate to the NVOnline portal. From the top navigation bar, select the appropriate Site for your company. Use the Content Library to access reference documents such as CAD files, platform design guides, and related specifications.

The screenshot displays the NVIDIA NVOnline Content Library interface. At the top, the NVIDIA logo and 'NVONLINE' text are on the left, while 'Site: MGX_Foxconn' and 'Tinker Tsai' are on the right. Below this is a navigation bar with 'HOME', 'BUG', and 'HELP' links. The main section is titled 'CONTENT LIBRARY' in a green header. A search bar with the placeholder 'Enter keywords here or apply filters below' and a 'SEARCH' button is present. On the left, a 'Filters' sidebar includes sections for 'Product Line' (with checkboxes for HGX and MGX), 'Content Class' (with a checkbox for Platform), 'Product Family' (with checkboxes for GB200 NVL, HGX B100, and HGX B200), and 'HW Platform/SW Release'. The main content area shows a list of documents with their titles, posting dates, and download links. The documents listed are: 'MGX GB200 Bianca Cold Plate CAD and Thermal Test S...', 'GB200 MGX Rack Mounting Kit for CC and Manifold, L...', 'NVIDIA Blackwell HGX 8-GPU Platform Design Guide', and 'MGX GB200 FullRack 44RU Manifold CAD'. The footer contains links for 'Privacy Policy', 'Manage My Privacy', 'Do Not Sell or Share My Data', 'Accessibility', 'Corporate Policies', 'Product Security', and 'Terms of Use', along with the copyright notice 'Copyright © 2024 NVIDIA Corporation.'

Step 2: Navigate to Report a Bug

From the NVOnline homepage, click on the “Bug” menu in the top navigation bar and select “Report a Bug” from the dropdown menu.

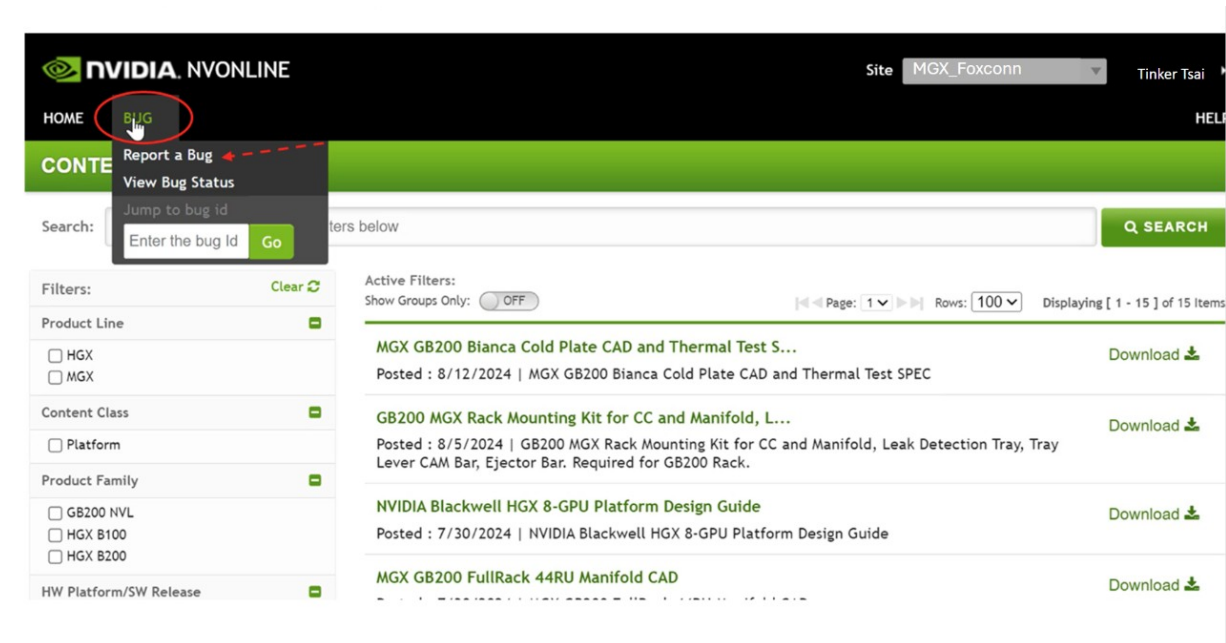

Step 3: Fill in the Bug Report Form

Complete the “Report a Bug” form. The form fields are the same for both Qualification Review and RFI submissions, with differences only in the Synopsis and Focus Area fields as noted below.

Please follow the template below exactly. Otherwise, there may be delays in processing your submission. Replace all placeholders with your information and remove the angle brackets <>.

Leave “DC Infrastructure CDU Review” and “DC Infrastructure CDU RFI” unchanged.

Common Form Fields

- > **Problem Type:** Select “Qualification Review” from the dropdown.
- > **Severity:** Low
- > **Priority:** 3 - Low
- > **Divisions:** Select your company site from the dropdown.
- > **Issue Type:** Select “Qualification-Review-Issue”.

- > **Product Segment:** Select “Other”.
- > **Focus Area:** Select “DC Infrastructure”.

Synopsis Format by Use Case

The **Synopsis** field (200 characters maximum) must follow one of these formats depending on the use case:

- > **Qualification Review:** Facilities Level - **<Name>** DC Infrastructure **CDU Review**
- > **Request for Information (RFI):** Facilities Level - **<Name>** DC Infrastructure **CDU RFI**

Use RFI only for pre-qualification questions. For formal qualification submissions, use Review.

NVIDIA NVONLINE Site [] []

HOME BUG

REPORT A BUG

Issue Type

Issue Details

Product Details

Additional Information

Attachments

***Problem Type** Qualification Review **Severity** Low **Priority** 3 - Low **Fix Needed in PROD by** mm/dd/yyyy

***Synopsis**

200 characters remaining (200 maximum)

***Description**

***** Instructions for NVQual-Review-Issue *****

1. Select the appropriate product segment, issue type.

2. For OEM/ODMs, please attach all logs and results in the latest PVP Checklist (*.xslm)

3. For IBVs, please attach NVSVT logs for submission

***Divisions:** [] ***Products:** [] ***Operating Systems:** []

- Projects

Select or Edit []

+ Cc Details

- Customer Keyword Details

Select or Edit []

- Meta Data Information

***Issue Type** Qualification-Review-Issue

***Product Segment**

☐ MGX Products

☐ HGX GPU Baseboards

☐ Networking Products

☐ PCIe Datacenter

☐ PCIe ProViz

☐ Other

***Focus Area**

☐ PVP (NVQual v2.x)

☐ NVQual v1.0

☐ DC Infrastructure

☐ MGX AVL/RVL

☐ MissionControl Validation

- Attachments

Show details

Drag and Drop 1 or more files or Browse to Select

Submit Bug **Save as draft** **Cancel**

Step 4: Enter CDU-Specific Description (Qualification Review)

For Qualification Review submissions, enter the following information in the **Description** field. Items marked with **<attachment>** must be uploaded as file attachments:

Subject: Facilities Level - <Supplier Company Name> DC Infrastructure CDU Review

MPN: <Supplier Part Number>

Revision: <Version>

SPEC: Supplier SPEC <Attachment>

3D CAD: Supplier CAD <Attachment>

2D Drawing: Supplier 2D <Attachment>

Self Qualification Report: Supplier performance qualification report. Template on PID: CDU Self Qualification Guideline <Attachment>

Product Name: <Name>

Product Webpage: <URL>

1. Subject: Facilities Level - <Supplier Company Name> DC Infrastructure **CDU** Review
2. MPN: <Supplier part number>
3. Revision: <version>
4. SPEC: Supplier SPEC **<attachment>**
5. 3D CAD: Supplier CAD **<attachment>**
6. 2D Drawing: Supplier 2D **<attachment>**
7. Self Qualification Report: Supplier performance validation report. Template on PID: **CDU Self Qualification Guideline <attachment>**
8. Product Name: <Name>
9. Product Webpage: <URL>

Step 4 (Alternate): Enter CDU Description for RFI

For Request for Information (RFI) submissions, enter your questions or clarification requests in the Description field. Delete the default template text in the field and write your specific questions. Select “DC Infrastructure” as the Focus Area. Attach any supporting documentation as needed.

Step 5: Add Members, Upload Attachments, and Submit

Before submitting the bug, complete the following:

Add Members: In the Cc Details section, add all relevant NVIDIA and partner team members who should be notified of this submission.

Upload Attachments: In the Attachments section, drag and drop or browse to upload all design files referenced in the description (SPEC, 3D CAD, 2D Drawing, Self Qualification Report). For RFI submissions, attach any supporting documents related to your questions.

Submit: Once all details are filled in and attachments are uploaded, click the “Submit Bug” button. You may also use “Save as draft” to save your progress before submitting.

The screenshot shows the NVIDIA NVONLINE 'REPORT A BUG' form. The form is divided into several sections:

- Issue Type:** A dropdown menu with 'Qualification Review' selected.
- Severity:** A dropdown menu with 'Low' selected.
- Priority:** A dropdown menu with '3 - Low' selected.
- Fix Needed in PROD by:** A date input field with the placeholder 'mm/dd/yyyy'.
- Synopsis:** A text area with a 200-character limit.
- Description:** A rich text editor with a toolbar and a text area containing instructions for PVP / NVIDIA Qualified Submission.
- Divisions:** A dropdown menu with 'Projects' selected.
- Products:** A text input field.
- Operating Systems:** A text input field.
- Issue Type:** A dropdown menu with 'Qualification-Review-Issue' selected.
- Product Segment:** A list of radio buttons for MGX Products, HGX GPU Baseboards, Networking Products, PCIe Datacenter, PCIe ProViz, and Other.
- Focus Area:** A list of radio buttons for PVP (NVIDIA Qualified), DC Infrastructure, MGX AVL/RVL, and MissionControl Validation.
- Attachments:** A section with a 'Show details' link and a file upload area.

At the bottom of the form, there are three buttons: 'Submit Bug', 'Save as draft', and 'Cancel'.

After submission, you can add comments and upload additional attachments through the Comments section:

Comments

Format
Font
Size
A
A
B
I
U
S
“
”
T
X
:
=
≡
≡
≡
≡
≡
≡
≡
≡

body

Visibility:
☒ NVIDIA Private
☐ Customer viewable


Step 6: View Bug Status and Add Comments

After submitting, you can track your submission and provide additional information:

View Bug Status: Navigate to Bug > “View Bug Status” in the top menu. Search by Bug ID, synopsis, or other criteria. Click on the Bug ID to view full details.

Add Comments: From the bug detail page, scroll to the Comment Log section and click “Add Comment” to upload additional attachments or provide updates.

All information submitted is confidential and only viewable between the submitting partner and NVIDIA.



NVBug Notifications

Users will receive system notifications (via email) whenever there is an update on their NVBug submission. These notifications include status changes, new comments, and resolution updates. This applies to both Qualification Review and RFI submissions.

Flushing Procedure

Executive Summary

Liquid cooling systems can encounter contamination issues that compromise their efficiency and longevity. Biological growth, often stemming from insufficient biocide levels or water ingress, can lead to clogs and diminished heat transfer. Regular monitoring and biocide maintenance are vital to prevent this.

Additionally, metal corrosion within the loop introduces metallic contaminants, necessitating the use of corrosion inhibitors and compatible components. Dust and particles can obstruct flow and reduce cooling efficiency, requiring regular filtration and cleaning of system components. Chemical contaminants, whether from manufacturing residues or impurities in the coolant, pose risks that can be mitigated by using high-quality coolant and thorough component flushing before assembly.

To maintain optimal performance, liquid cooling systems demand proactive upkeep, adherence to manufacturer guidelines, and vigilance in detecting and resolving issues promptly. By implementing these measures, users can minimize the risk of contamination and preserve the efficiency and longevity of their liquid cooling systems.


1. Flushing needs to be performed twice before sending it to the customer deployment site.
2. Connect the secondary supply and return the hose directly and then circulate the coolant within the heat exchanger.
3. For flushing, a filter of 5 microns needs to be used for the entire flushing procedure.
4. Secondary loop filters need to be installed, and the maximum filter size should not exceed 5 microns.
5. Fill the heat exchanger with PG-25.
 - a. Must meet the following requirements:
 - i. pH: 8 - 10.5 (ASTM D1287)
 - ii. Reserve Alkalinity: > 4 ml based on the fluid as is (ASTM D1121)
 - iii. Copper: < 2 ppm (ASTM D6310)
 - iv. Iron: < 2 ppm (ASTM D6310)
 - v. Total Hardness: < 100 ppm (ASTM D6310)
 - vi. Chloride: < 25 ppm (ASTM D5827)
 - vii. Sulfate: < 25 ppm (ASTM D5827)
 - viii. **Fluids that meet these requirements can be found [here](#)

- ix. If using any other PG-25 products, confirm with the NVIDIA DC Engineering team first.
6. Switch ON the heat exchanger and circulate the coolant for the 2 hours at maximum flow rate of the heat exchanger.
7. After the first circulation, flush the coolant and collect the coolant samples for lab testing and remove the filters.
8. Inspect the filters and if those are dirty clean it before reusing it for a second flush or use a new filter.
9. Repeat the these steps for the second flushing step.
10. Make sure before sending the heat exchanger to the customer, filters and internal hoses are clean.
11. Once the heat exchanger is flushed according to the mentioned steps, install the filter as requested by customer.
12. Follow the shipping instructions as mentioned in the following steps and include flushing reports with CDU SN and label information.

Detailed Flushing Steps

To ensure a contamination-free CDU, follow the flushing steps carefully and make sure to repeat the process twice before shipping the CDU for deployment.


Figure 1. Flushing Steps

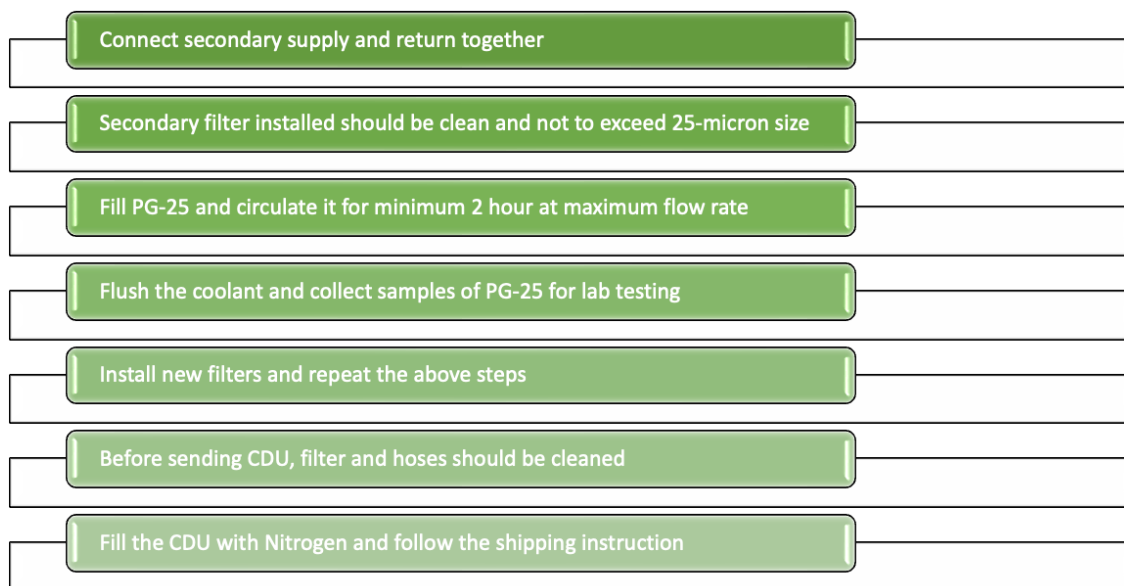

Filter Initial Inspection

It is essential to examine and clean the filters before filling the unit with coolant since most of the contaminants are typically stuck in the filter. The required filter size is 25 microns (550 meshes). Make sure to inspect the inside of the filter for contaminants as well.


Figure 2. Filter Inspection



Looping and Charging

Once the filters have been securely reinstalled, the unit should be connected in a loop configuration using a dedicated hose. This involves connecting the unit coolant supply port to the return port in a loop fashion.

Figure 3. Connecting Unit Coolant Supply Port

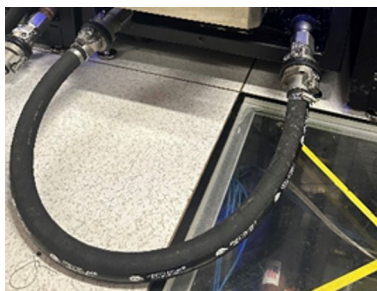

Flushing with Coolant

- > After the unit is fully charged while looped to itself, pumps can be turned on at low speed (less than 30% of full speed).
- > Make sure that the charging system is still active, so that more coolant is pumped into the unit as air bubbles bleed out from the internal vents.
- > Whenever there is no air left in the system, operate the CDU at maximum flow rate (for an hour at least, if possible) to flush it properly.

Draining and Inspecting

- > The samples of the drained coolant should be taken for lab inspection.
- > Monitor and measure the drained coolant volume. Comparing it with the initial fluid charge will indicate the residual fluid in the unit. This will indicate how much fluid is remaining in the CDU.

Notice

This document is provided for information purposes only and shall not be regarded as a warranty of a certain functionality, condition, or quality of a product. NVIDIA Corporation ("NVIDIA") makes no representations or warranties, expressed or implied, as to the accuracy or completeness of the information contained in this document and assumes no responsibility for any errors contained herein. NVIDIA shall have no liability for the consequences or use of such information or for any infringement of patents or other rights of third parties that may result from its use. This document is not a commitment to develop, release, or deliver any Material (defined below), code, or functionality.

NVIDIA reserves the right to make corrections, modifications, enhancements, improvements, and any other changes to this document, at any time without notice.

Customer should obtain the latest relevant information before placing orders and should verify that such information is current and complete.

NVIDIA products are sold subject to the NVIDIA standard terms and conditions of sale supplied at the time of order acknowledgement, unless otherwise agreed in an individual sales agreement signed by authorized representatives of NVIDIA and customer ("Terms of Sale"). NVIDIA hereby expressly objects to applying any customer general terms and conditions with regards to the purchase of the NVIDIA product referenced in this document. No contractual obligations are formed either directly or indirectly by this document.

NVIDIA products are not designed, authorized, or warranted to be suitable for use in medical, military, aircraft, space, or life support equipment, nor in applications where failure or malfunction of the NVIDIA product can reasonably be expected to result in personal injury, death, or property or environmental damage. NVIDIA accepts no liability for inclusion and/or use of NVIDIA products in such equipment or applications and therefore such inclusion and/or use is at customer's own risk.

NVIDIA makes no representation or warranty that products based on this document will be suitable for any specified use. Testing of all parameters of each product is not necessarily performed by NVIDIA. It is customer's sole responsibility to evaluate and determine the applicability of any information contained in this document, ensure the product is suitable and fit for the application planned by customer, and perform the necessary testing for the application in order to avoid a default of the application or the product. Weaknesses in customer's product designs may affect the quality and reliability of the NVIDIA product and may result in additional or different conditions and/or requirements beyond those contained in this document. NVIDIA accepts no liability related to any default, damage, costs, or problem which may be based on or attributable to: (i) the use of the NVIDIA product in any manner that is contrary to this document or (ii) customer product designs.

No license, either expressed or implied, is granted under any NVIDIA patent right, copyright, or other NVIDIA intellectual property right under this document. Information published by NVIDIA regarding third-party products or services does not constitute a license from NVIDIA to use such products or services or a warranty or endorsement thereof. Use of such information may require a license from a third party under the patents or other intellectual property rights of the third party, or a license from NVIDIA under the patents or other intellectual property rights of NVIDIA.

Reproduction of information in this document is permissible only if approved in advance by NVIDIA in writing, reproduced without alteration and in full compliance with all applicable export laws and regulations, and accompanied by all associated conditions, limitations, and notices.

THIS DOCUMENT AND ALL NVIDIA DESIGN SPECIFICATIONS, REFERENCE BOARDS, FILES, DRAWINGS, DIAGNOSTICS, LISTS, AND OTHER DOCUMENTS (TOGETHER AND SEPARATELY, "MATERIALS") ARE BEING PROVIDED "AS IS." NVIDIA MAKES NO WARRANTIES, EXPRESSED, IMPLIED, STATUTORY, OR OTHERWISE WITH RESPECT TO THE MATERIALS, AND EXPRESSLY DISCLAIMS ALL IMPLIED WARRANTIES OF NONINFRINGEMENT, MERCHANTABILITY, AND FITNESS FOR A PARTICULAR PURPOSE. TO THE EXTENT NOT PROHIBITED BY LAW, IN NO EVENT WILL NVIDIA BE LIABLE FOR ANY DAMAGES, INCLUDING WITHOUT LIMITATION ANY DIRECT, INDIRECT, SPECIAL, INCIDENTAL, PUNITIVE, OR CONSEQUENTIAL DAMAGES, HOWEVER CAUSED AND REGARDLESS OF THE THEORY OF LIABILITY, ARISING OUT OF ANY USE OF THIS DOCUMENT, EVEN IF NVIDIA HAS BEEN ADVISED OF THE POSSIBILITY OF SUCH DAMAGES. Notwithstanding any damages that customer might incur for any reason whatsoever, NVIDIA's aggregate and cumulative liability towards customer for the products described herein shall be limited in accordance with the Terms of Sale for the product.

Trademarks

NVIDIA, and the NVIDIA logo are trademarks and/or registered trademarks of NVIDIA Corporation in the U.S. and other countries. Other company and product names may be trademarks of the respective companies with which they are associated.

Copyright

© 2025 NVIDIA Corporation. All rights reserved.

